



## WEEKLY CONSTRUCTION UPDATE

|  |                                |                                     |
|--|--------------------------------|-------------------------------------|
| <b>Project Title:</b> Whitman 20-Inch Force Main Replacement<br>CWSRF - 6885 |                                | <b>Report #:</b> EP - 7-15-2022     |
| <b>Project Location:</b> Brockton, MA<br>and Whitman, MA                     | <b>From:</b> 7/11/2022         | <b>Week:</b> 13                     |
| <b>Client:</b> Whitman, MA   | <b>To:</b> 7/15/2022           | <b>Engineer Project #:</b> 279-1901 |
| <b>On-Site Engineer:</b> Bob Fitzgerald,<br>Environmental Partners           | <b>Contact:</b> (508) 776-7556 |                                     |
| <b>Contractor:</b> C. Naughton Corp.   |                                |                                     |

### CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had one crew on site this week continuing the water main installation on Auburn Street. They installed approximately 480 LF of new 12-inch DI water main, 5 gate valves and 2 hydrants along Auburn Street on Monday, 7/11 and Tuesday 7/12. Approximately 26% of the water main is complete on Auburn Street.
2. C. Naughton had a second crew on site this week continuing the sewer main installation on Auburn Street. They installed approximately 700 LF of new pipe along Auburn Street from Monday, 7/11 to Thursday, 7/14. Approximately 40% of the sewer main is complete on Auburn Street.
3. C. Naughton had a third crew on site on Thursday, 7/7 installing fire hydrants. They installed two fire hydrants, one at the Auburn Street Pump Station and another near Hogg Memorial Drive.
4. On Thursday, C. Naughton encountered a 15" RCP drain line in conflict with the proposed 20" PVC sewer main. C. Naughton removed and replaced this section of drain with new PVC pipe.
5. C. Naughton plans to continue work on Auburn Street all day Friday until 5:00 p.m. All trenches will be backfilled, compacted, and paved prior to leaving for the weekend.

### WEEK LOOK-AHEAD SCHEDULE:

1. C. Naughton will have two crews on site next week to continue installation of the 12-inch DI water main and 20-inch PVC sewer main on Auburn Street. C. Naughton plans on detouring traffic onto Beaver Street and Alger Street starting on Monday 7/18. A copy of C. Naughton's proposed detour plan is attached for reference. C. Naughton will maintain access for local residents and for emergency vehicles while the detour is on-going.

2. C. Naughton will remove the road closure at the Route 18 / Auburn St intersection. Traffic heading westbound on Auburn Street from Whitman will be detoured down Beaver Street, while traffic heading eastbound on Auburn Street from Brockton will be detoured down Alger Street.
3. Daily traffic updates to the Town's project website will be posted to alert residents of anticipated road-closures and detours.

## PROJECT PHOTOS



*Photo 1: Installation of 12-inch DI Water Main on Auburn Street*



*Photo 2: 15" RCP Drain Pipe Replacement with 15" PVC Pipe on Auburn Street*

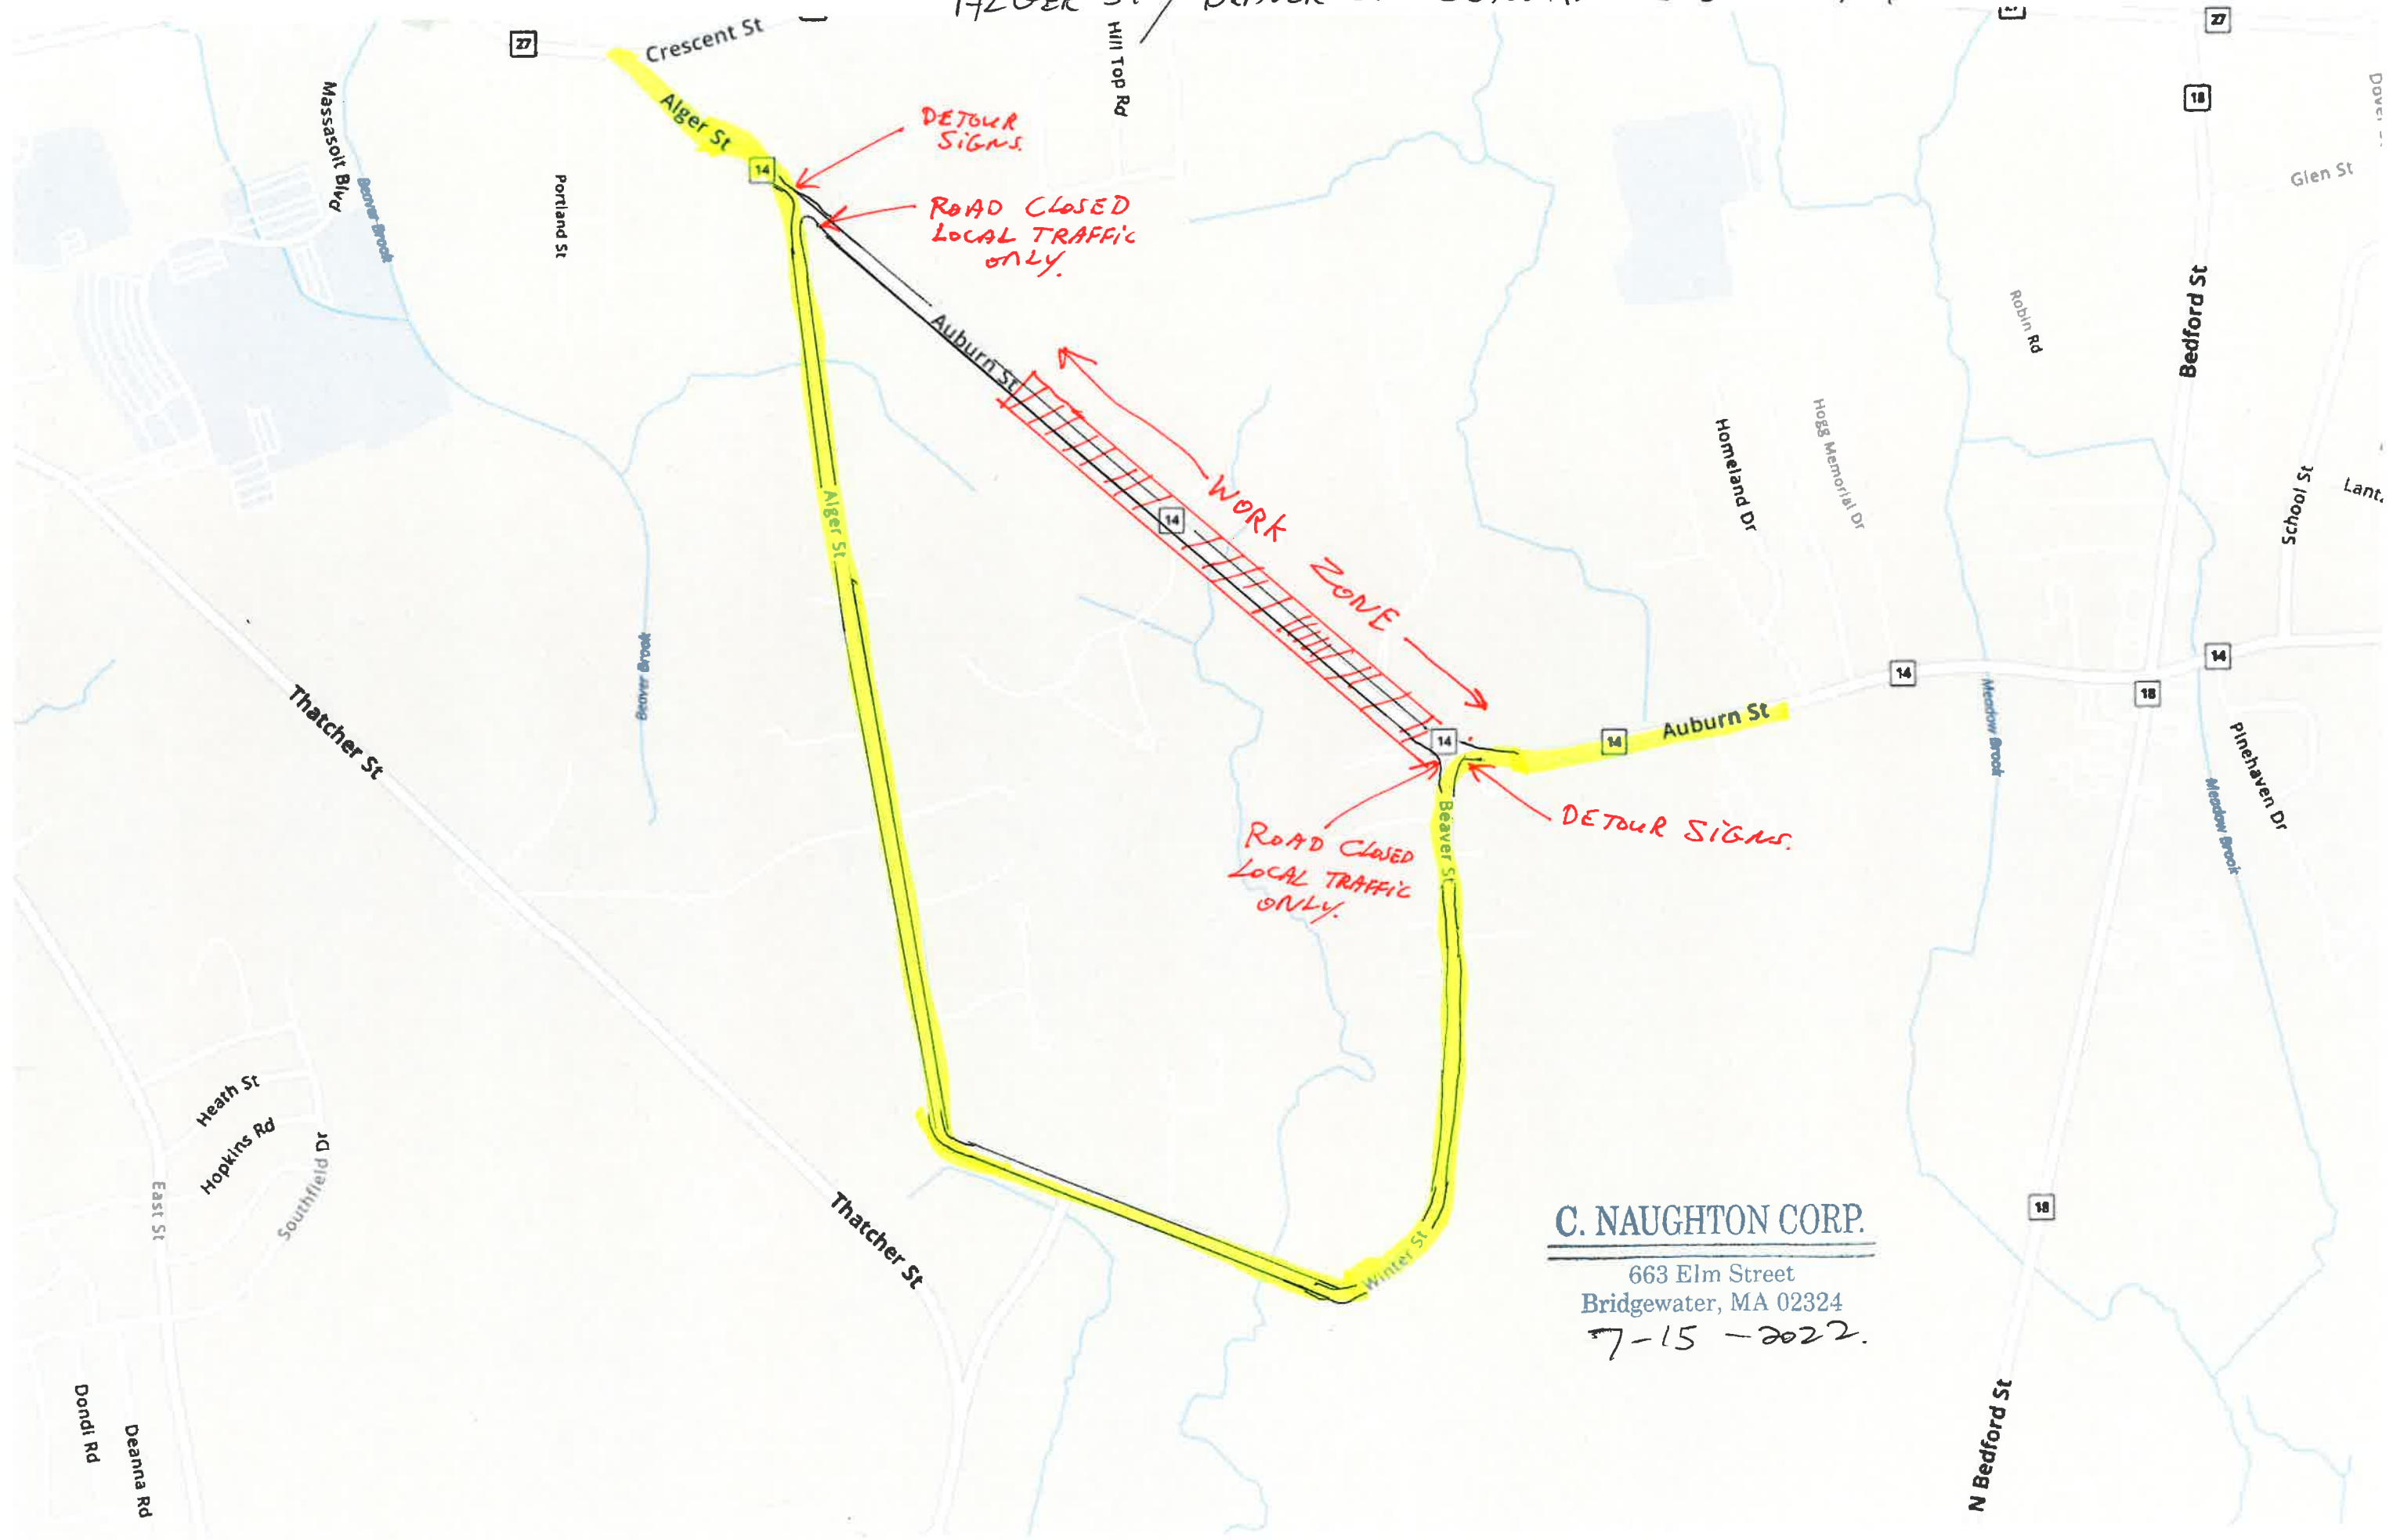


*Photo 3: Installation Valve Assembly on Auburn Street*

**Prepared By:** Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC

**Reviewed By:** Andrew Grota, Project Manager, Environmental Partners Group, LLC

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.



DETOUR SIGNS  
ROAD CLOSED LOCAL TRAFFIC ONLY.

WORK ZONE

ROAD CLOSED LOCAL TRAFFIC ONLY.

DETOUR SIGNS.

**C. NAUGHTON CORP.**  
663 Elm Street  
Bridgewater, MA 02324  
7-15-2022.
