



WEEKLY CONSTRUCTION UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885		Report #: EP - 7-22-2022
Project Location: Brockton, MA and Whitman, MA	From: 7/18/2022	Week: 14
Client: Whitman, MA	To: 7/22/2022	Engineer Project #: 279-1901
On-Site Engineer: Bob Fitzgerald, Environmental Partners	Contact: (508) 776-7556	
Contractor: C. Naughton Corp.		

CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had two crews on site this week; one crew continued the sewer force main installation on Auburn Street and the other installed water services on Auburn Street. They installed approximately 300 LF of new 20-inch PVC sewer force main, a 6' diameter air release manhole, and 4 water services along Auburn Street. Approximately 47% of the sewer force main is complete on Auburn Street.
2. C. Naughton detoured traffic onto Beaver Street and Alger Street while the sewer main work was on-going this week. A copy of the proposed detour plan is attached for reference.
3. C. Naughton dug a test pit to locate the 24" Brockton transmission water main on Tuesday 7/19. During excavation, an unmarked corporation stop was damaged and was repaired. C. Naughton crossed the 24" Brockton water transmission main on Thursday, 7/21 to continue their work up Auburn Street.
4. C. Naughton plans to continue work on Auburn Street on Friday 7/22. All trenches were backfilled, compacted, and paved prior to leaving for the weekend.

WEEK LOOK-AHEAD SCHEDULE:

1. C. Naughton will have two crews on site next week to continue installation of the service laterals pending confirmation of water main chlorination and 20-inch PVC sewer main on Auburn Street.
2. C. Naughton is maintaining a detour of Auburn Street while water and sewer work is on-going. C. Naughton will maintain access for local residents and for emergency vehicles while the detour is on-going.
3. Daily traffic updates to the Town's project website will be posted to alert residents of anticipated road closures and detours.

PROJECT PHOTOS



Photo 1: Installation of 20-inch PVC Sewer Force Main on Auburn Street




Photo 2: 20-inch PVC Sewer Force Main with 45 Degree Bend on Auburn Street



Photo 3: Trench Excavation at 45 Degree Bend

Prepared By: Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC


Reviewed By: Andrew Grotta, Project Manager, Environmental Partners Group, LLC

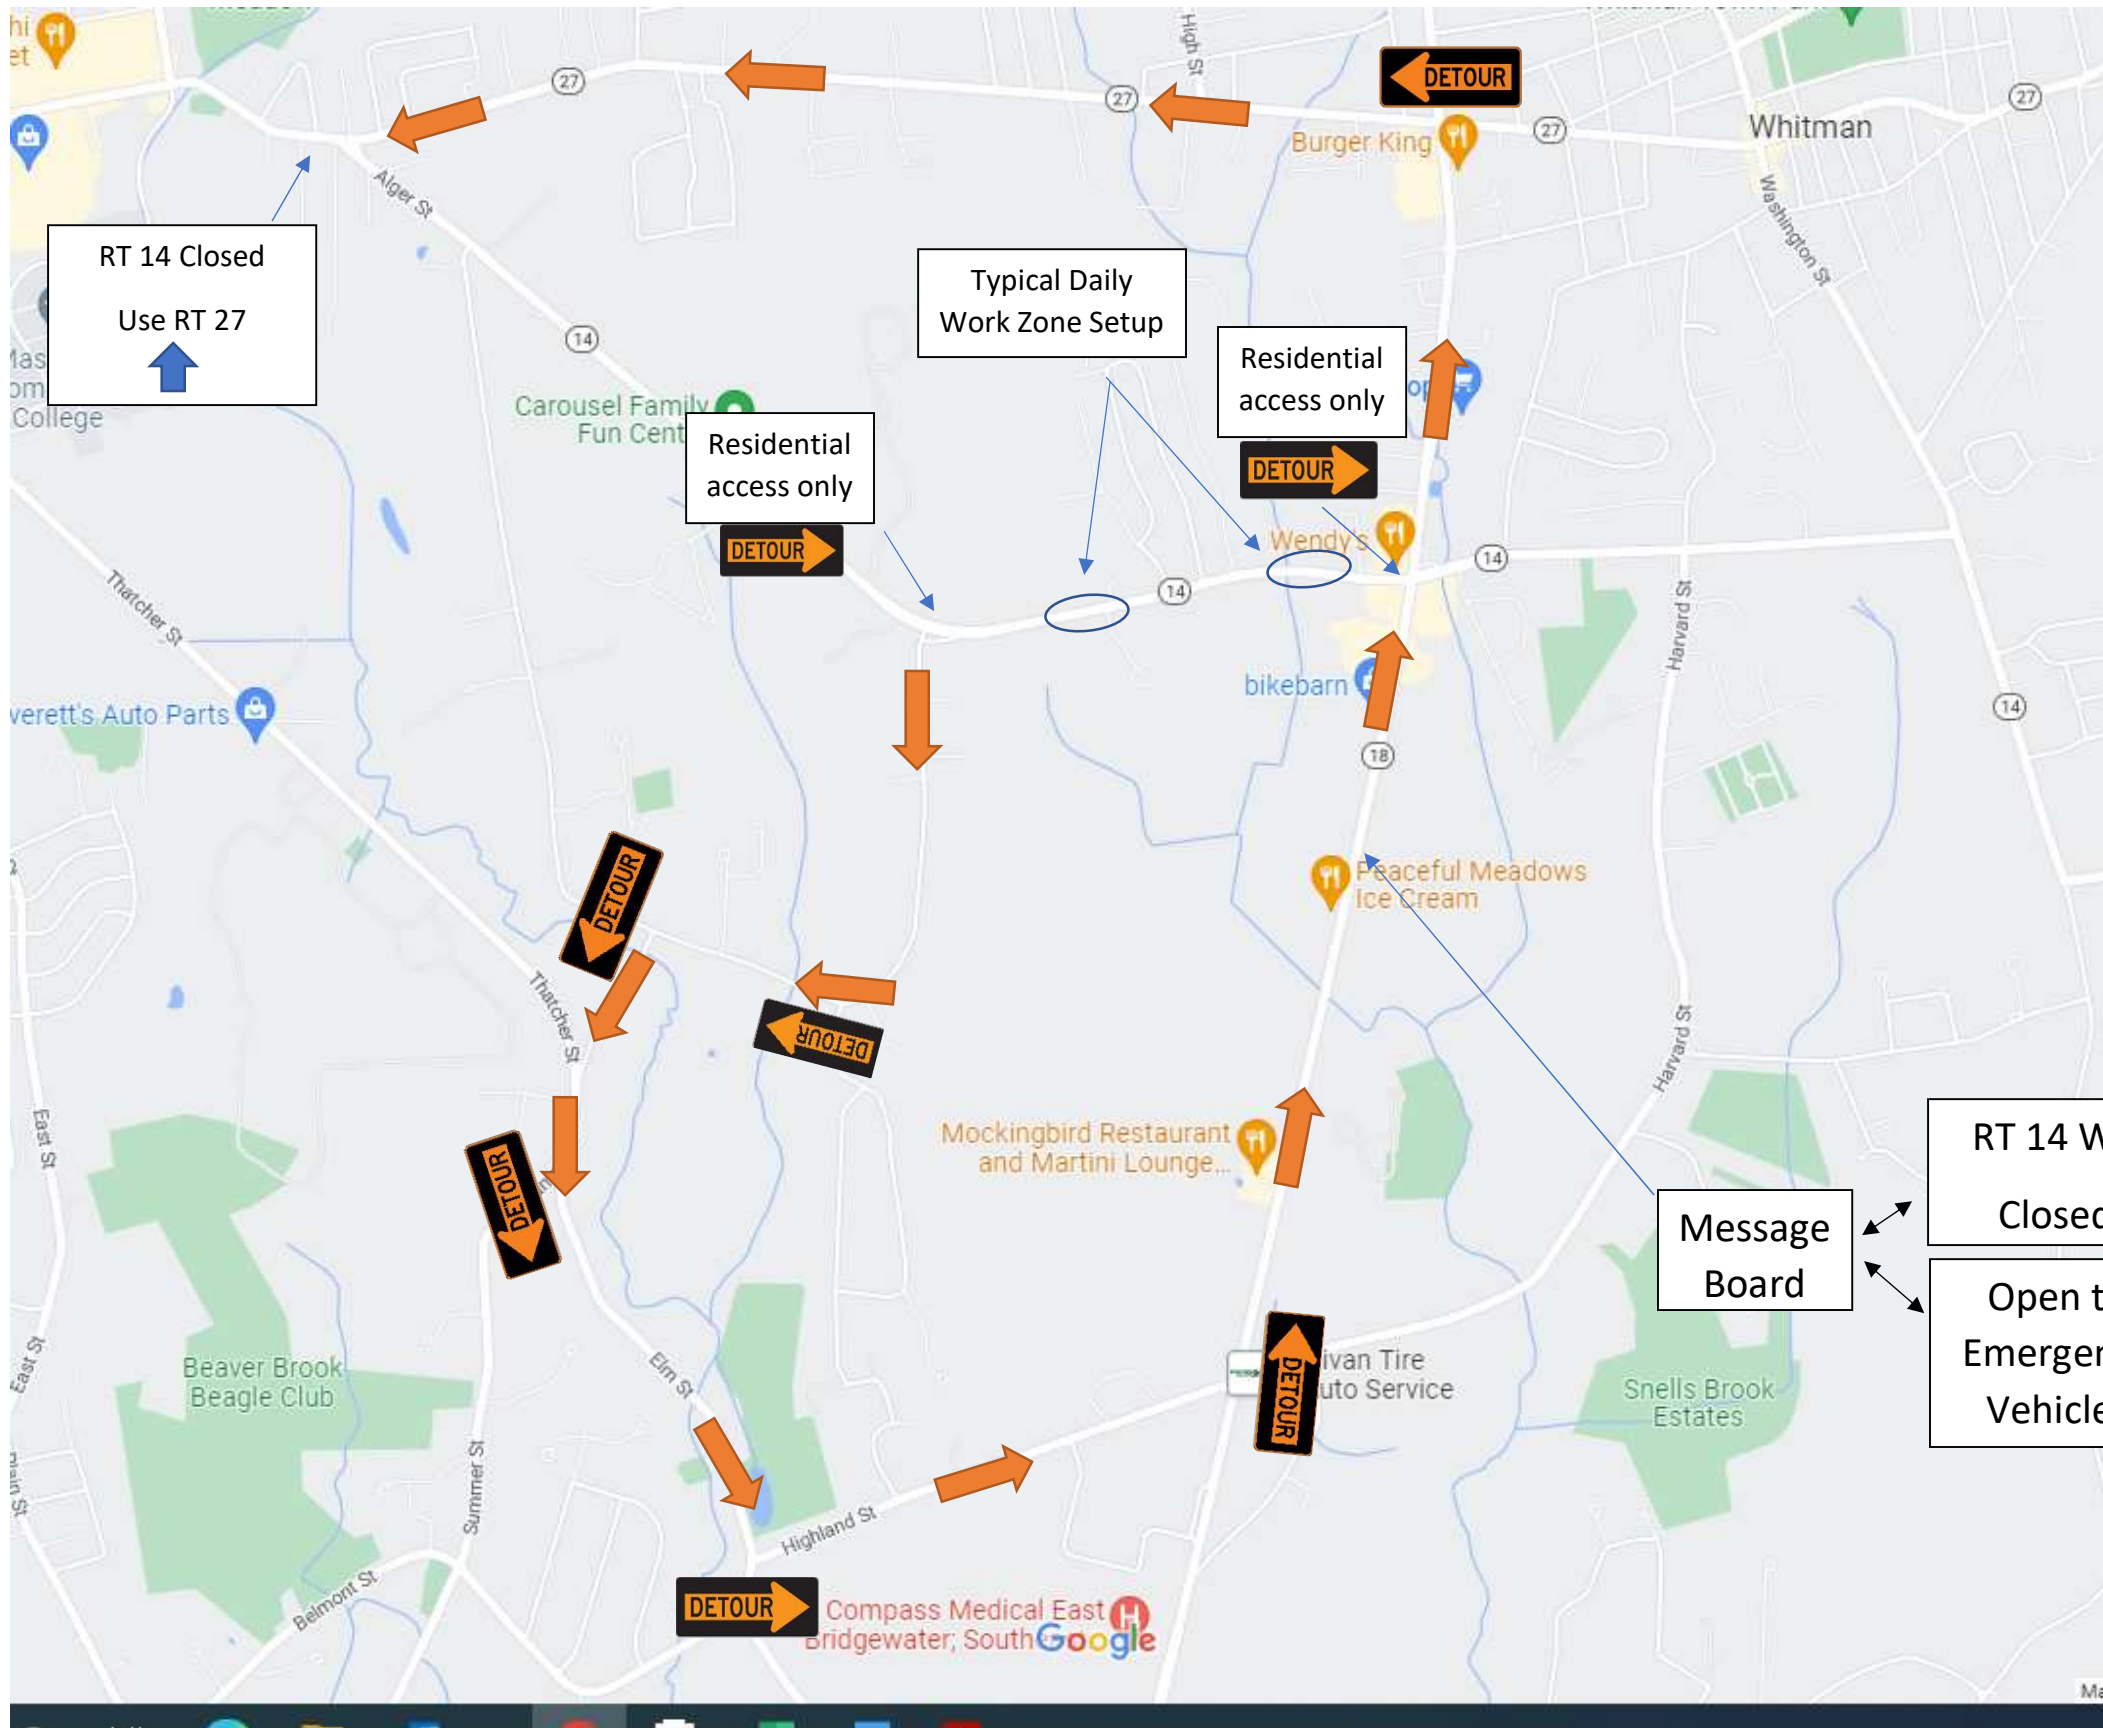

1. All construction signs per MassDOT MUTCD.
2. Work hours shall be 7am to 5pm.
3. C. Naughton Corp to order police details.



ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

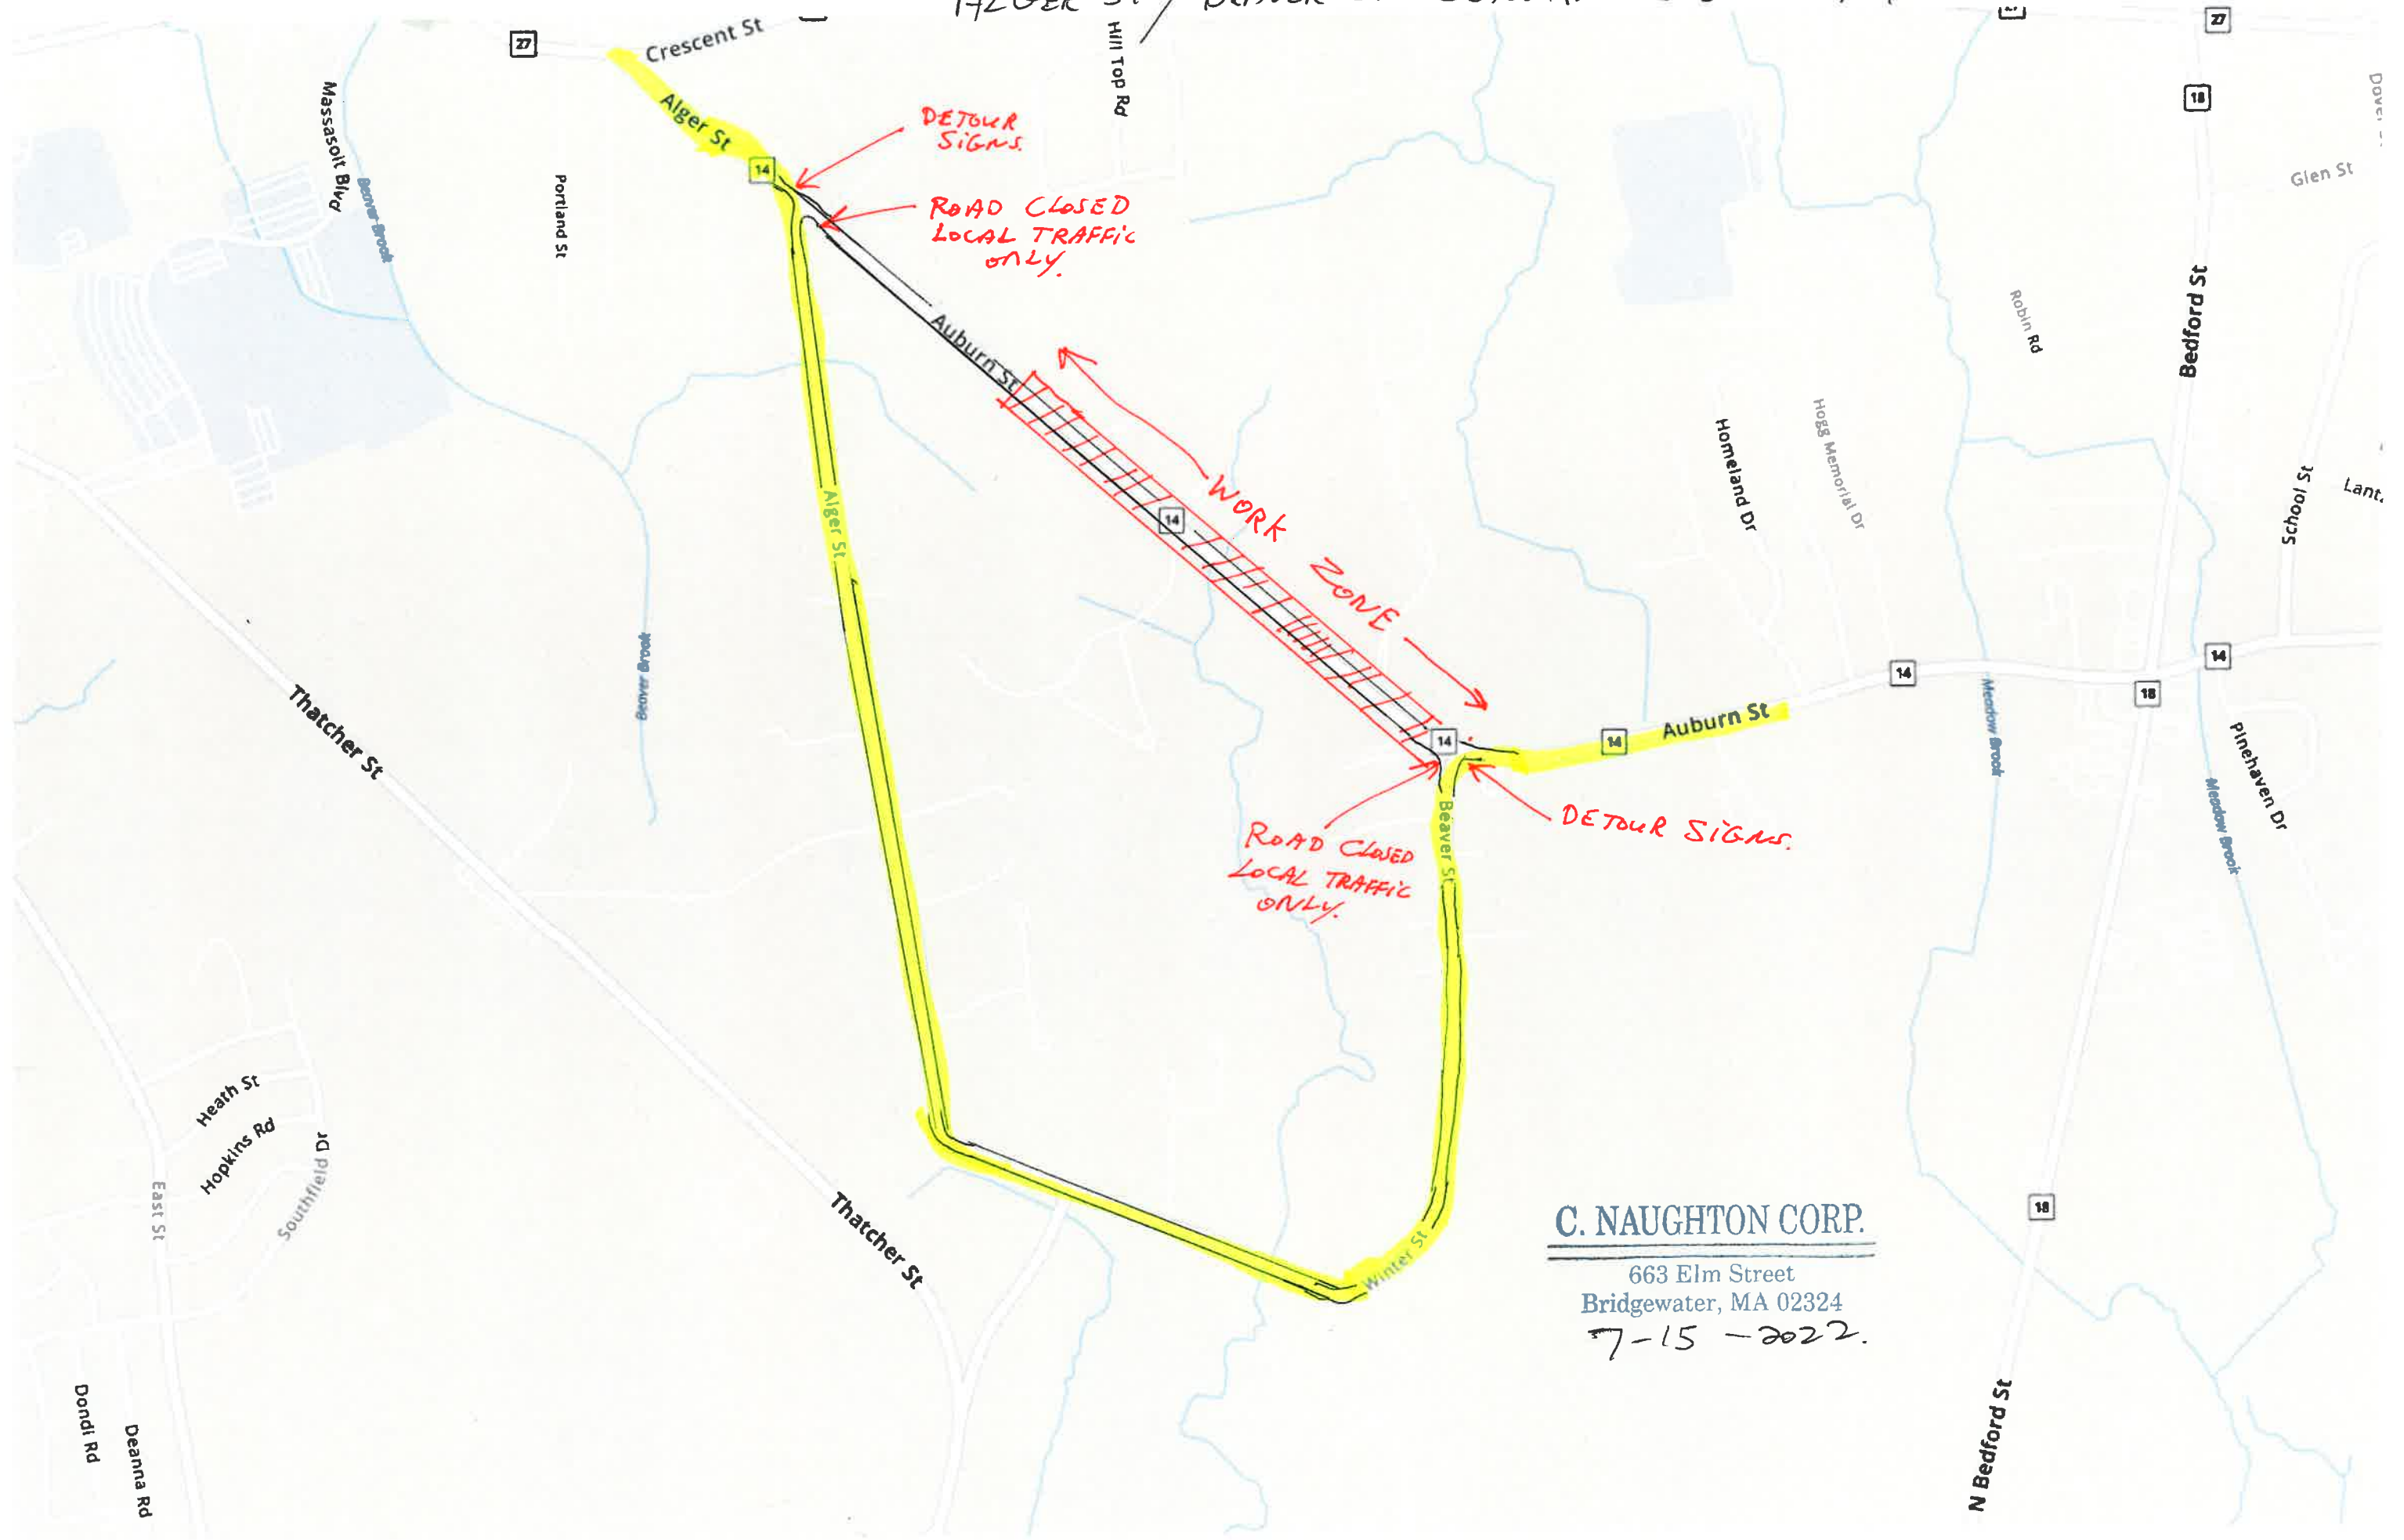

C. NAUGHTON CORP.
663 Elm Street
Bridgewater, MA 02324
7-15-2022.
