




DAILY WORK & TRAFFIC UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885	Date: 8-10-2022
Construction Location: Auburn Street, Whitman, MA	Construction hours: 7 A.M – 5 P.M.
<h3>ANTICIPATED WORK SCHEDULE AND TRAFFIC MANAGEMENT:</h3>	
<ol style="list-style-type: none"> 1. C. Naughton has two crews working on Auburn Street today; one crew will be working on Auburn Street disassembling the water bypass line from Hogg Memorial to Eliot Woods. The other crew will be continuing the installation of the 20" PVC sewer force main by #1129 Auburn Street. 2. Auburn Street will be closed in between Alger Street and Beaver Street for the installation of the 20" sewer force main, other than for local traffic and emergency vehicles. Traffic Management Plans showing the detour routes is attached. 3. Work is expected to take place from 7:00 a.m. until 5:00 p.m. All trenches will be backfilled and paved before leaving for the day. 	
<p>Prepared By: <u>Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC</u> Reviewed By: <u>Andrew Grota, Project Manager, Environmental Partners Group, LLC</u></p>	

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

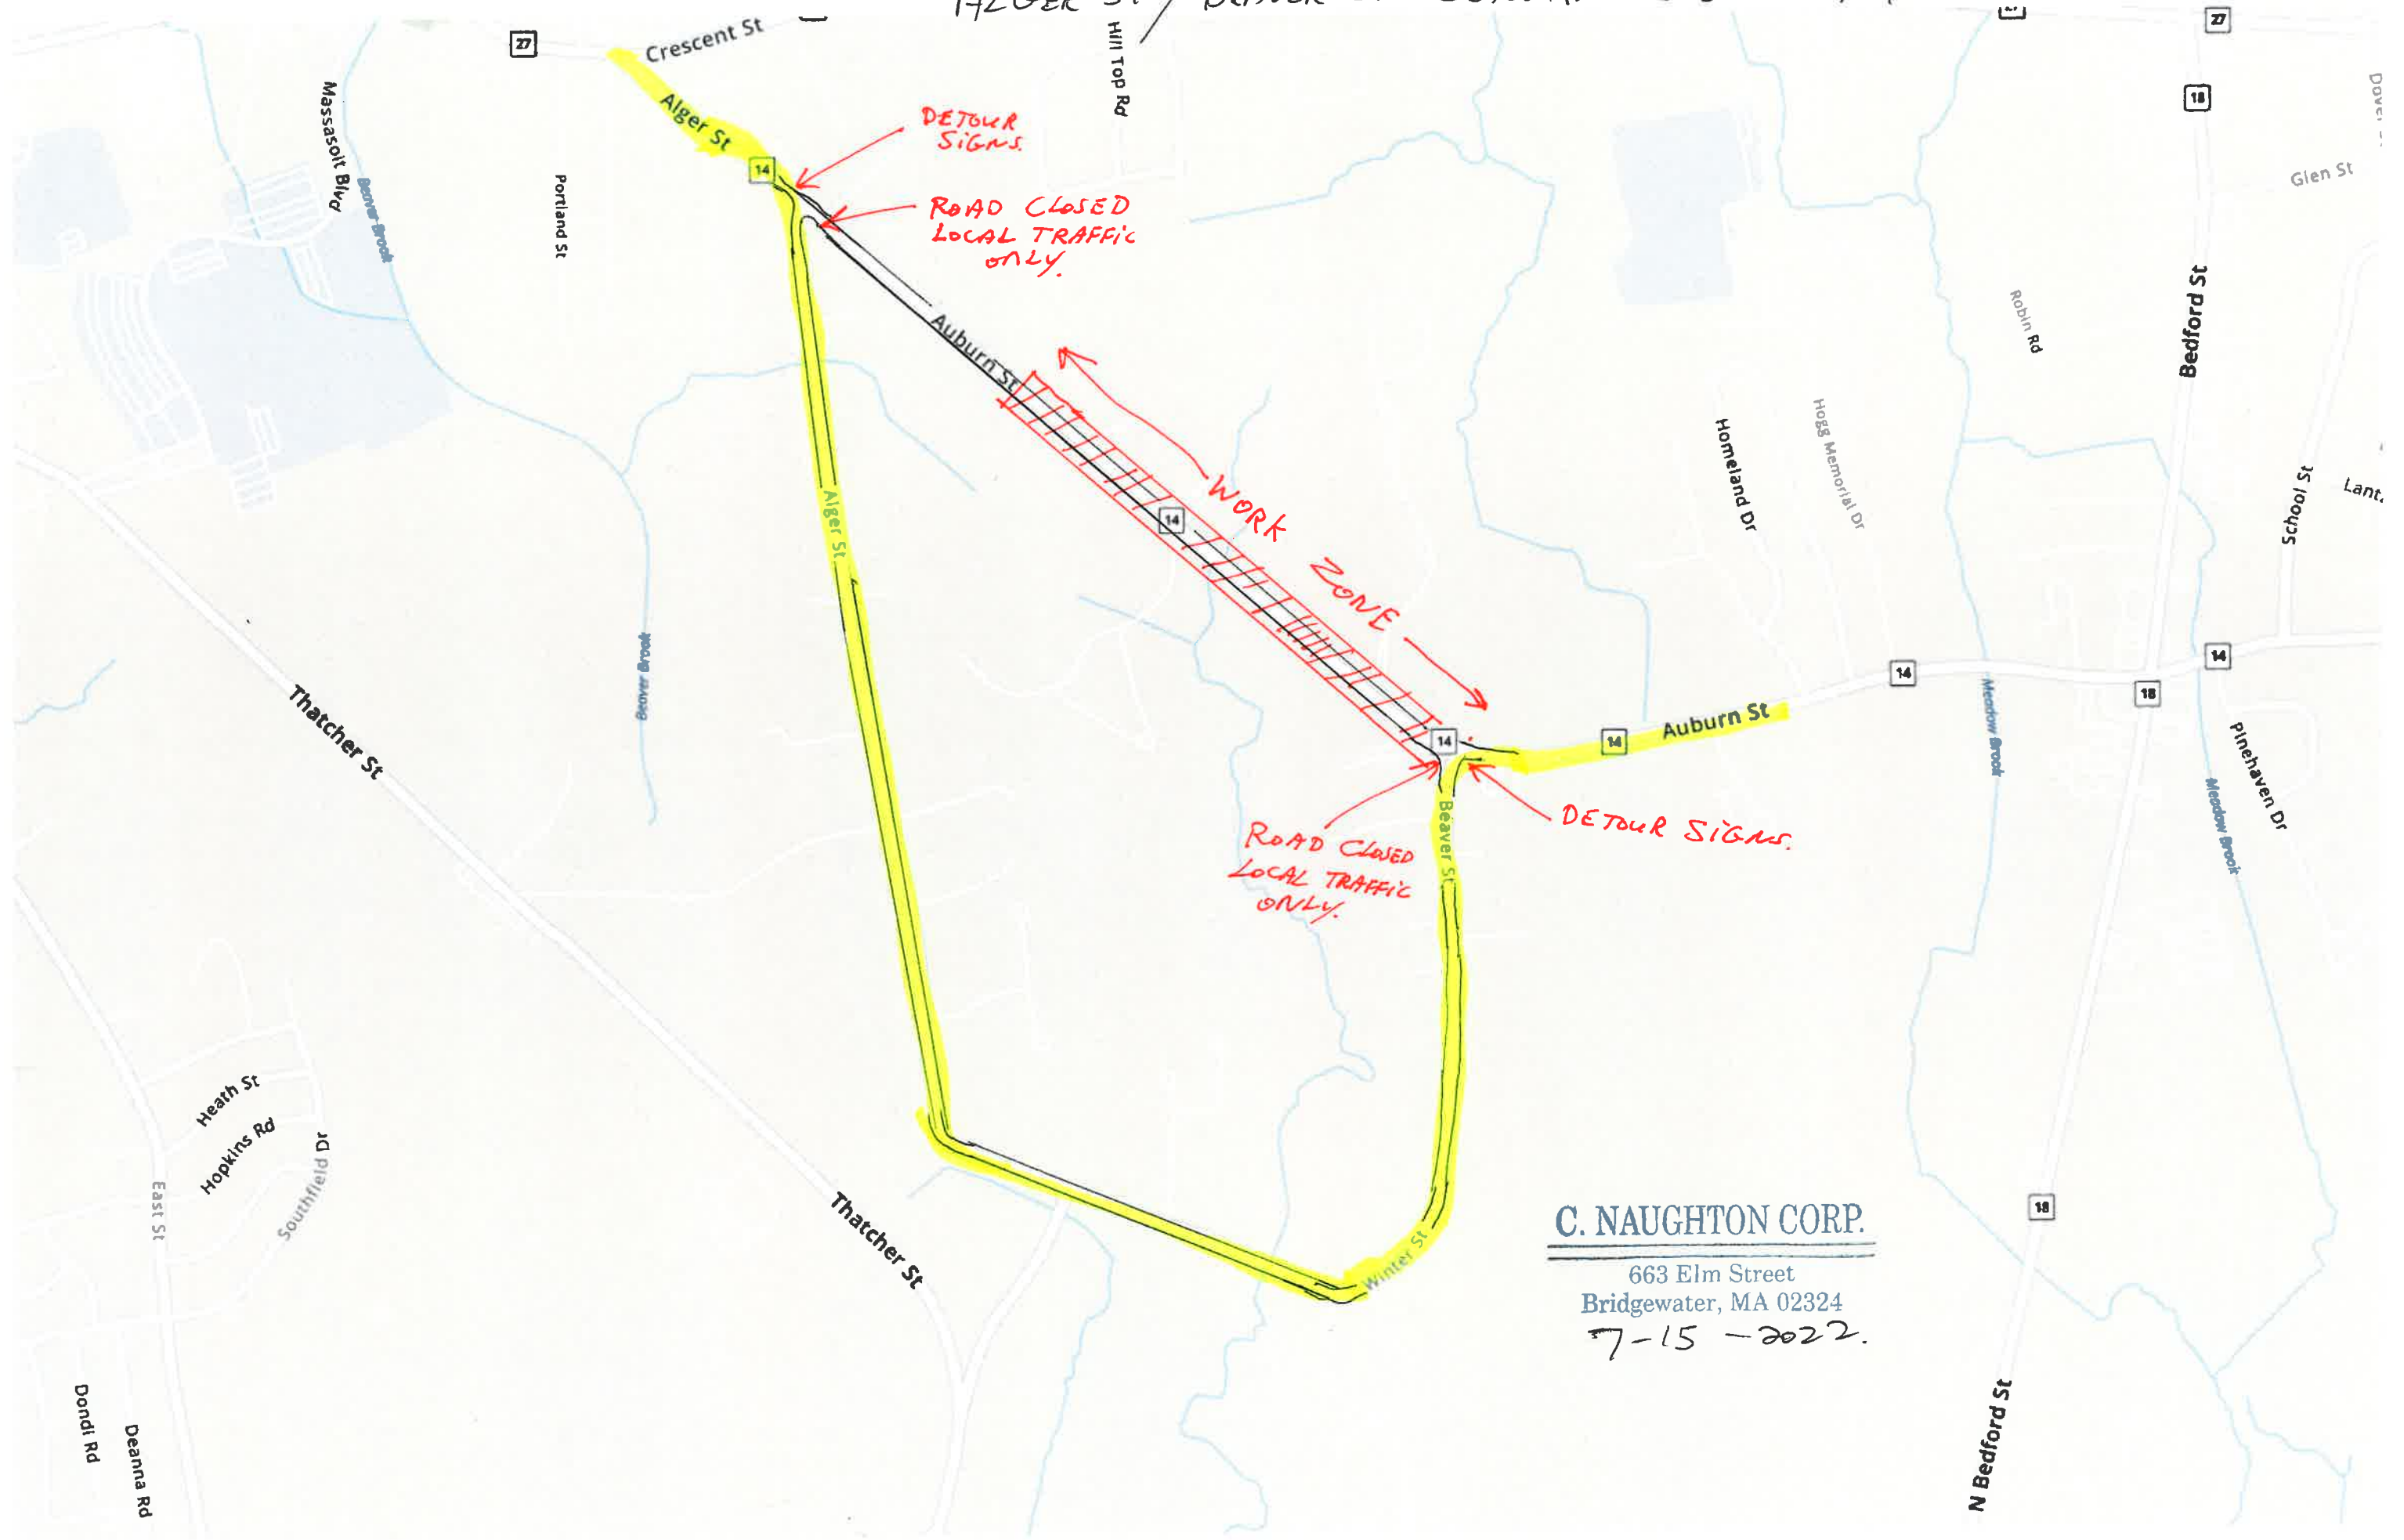

DETOUR SIGNS
ROAD CLOSED LOCAL TRAFFIC ONLY.

WORK ZONE

ROAD CLOSED LOCAL TRAFFIC ONLY.

DETOUR SIGNS.

C. NAUGHTON CORP.
663 Elm Street
Bridgewater, MA 02324
7-15-2022.
