




DAILY WORK & TRAFFIC UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885	Date: 8-15-2022 - 8-19-2022
Construction Location: Auburn Street, Whitman, MA	Construction hours: 7 A.M - 5 P.M.
<h3>ANTICIPATED WORK SCHEDULE AND TRAFFIC MANAGEMENT:</h3>	
<ol style="list-style-type: none"> 1. C. Naughton has two crews installing the 20" PVC sewer force main and the 12" DI water main on Auburn Street this week towards Alger Street. 2. Auburn Street will be closed in between Alger Street and Beaver Street for the installation of the 20" sewer force main, other than for local traffic and emergency vehicles. Traffic Management Plans showing the detour routes is attached. 3. Work is expected to take place from 7:00 a.m. until 5:00 p.m. All trenches will be backfilled and paved before leaving for the day. 4. Please note, the emergency access gate located at the rear of the middle school parking lot will be closed for public access at the end of the week on Friday, 8/19. 	
Prepared By: <u>Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC</u> Reviewed By: <u>Andrew Grota, Project Manager, Environmental Partners Group, LLC</u>	

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

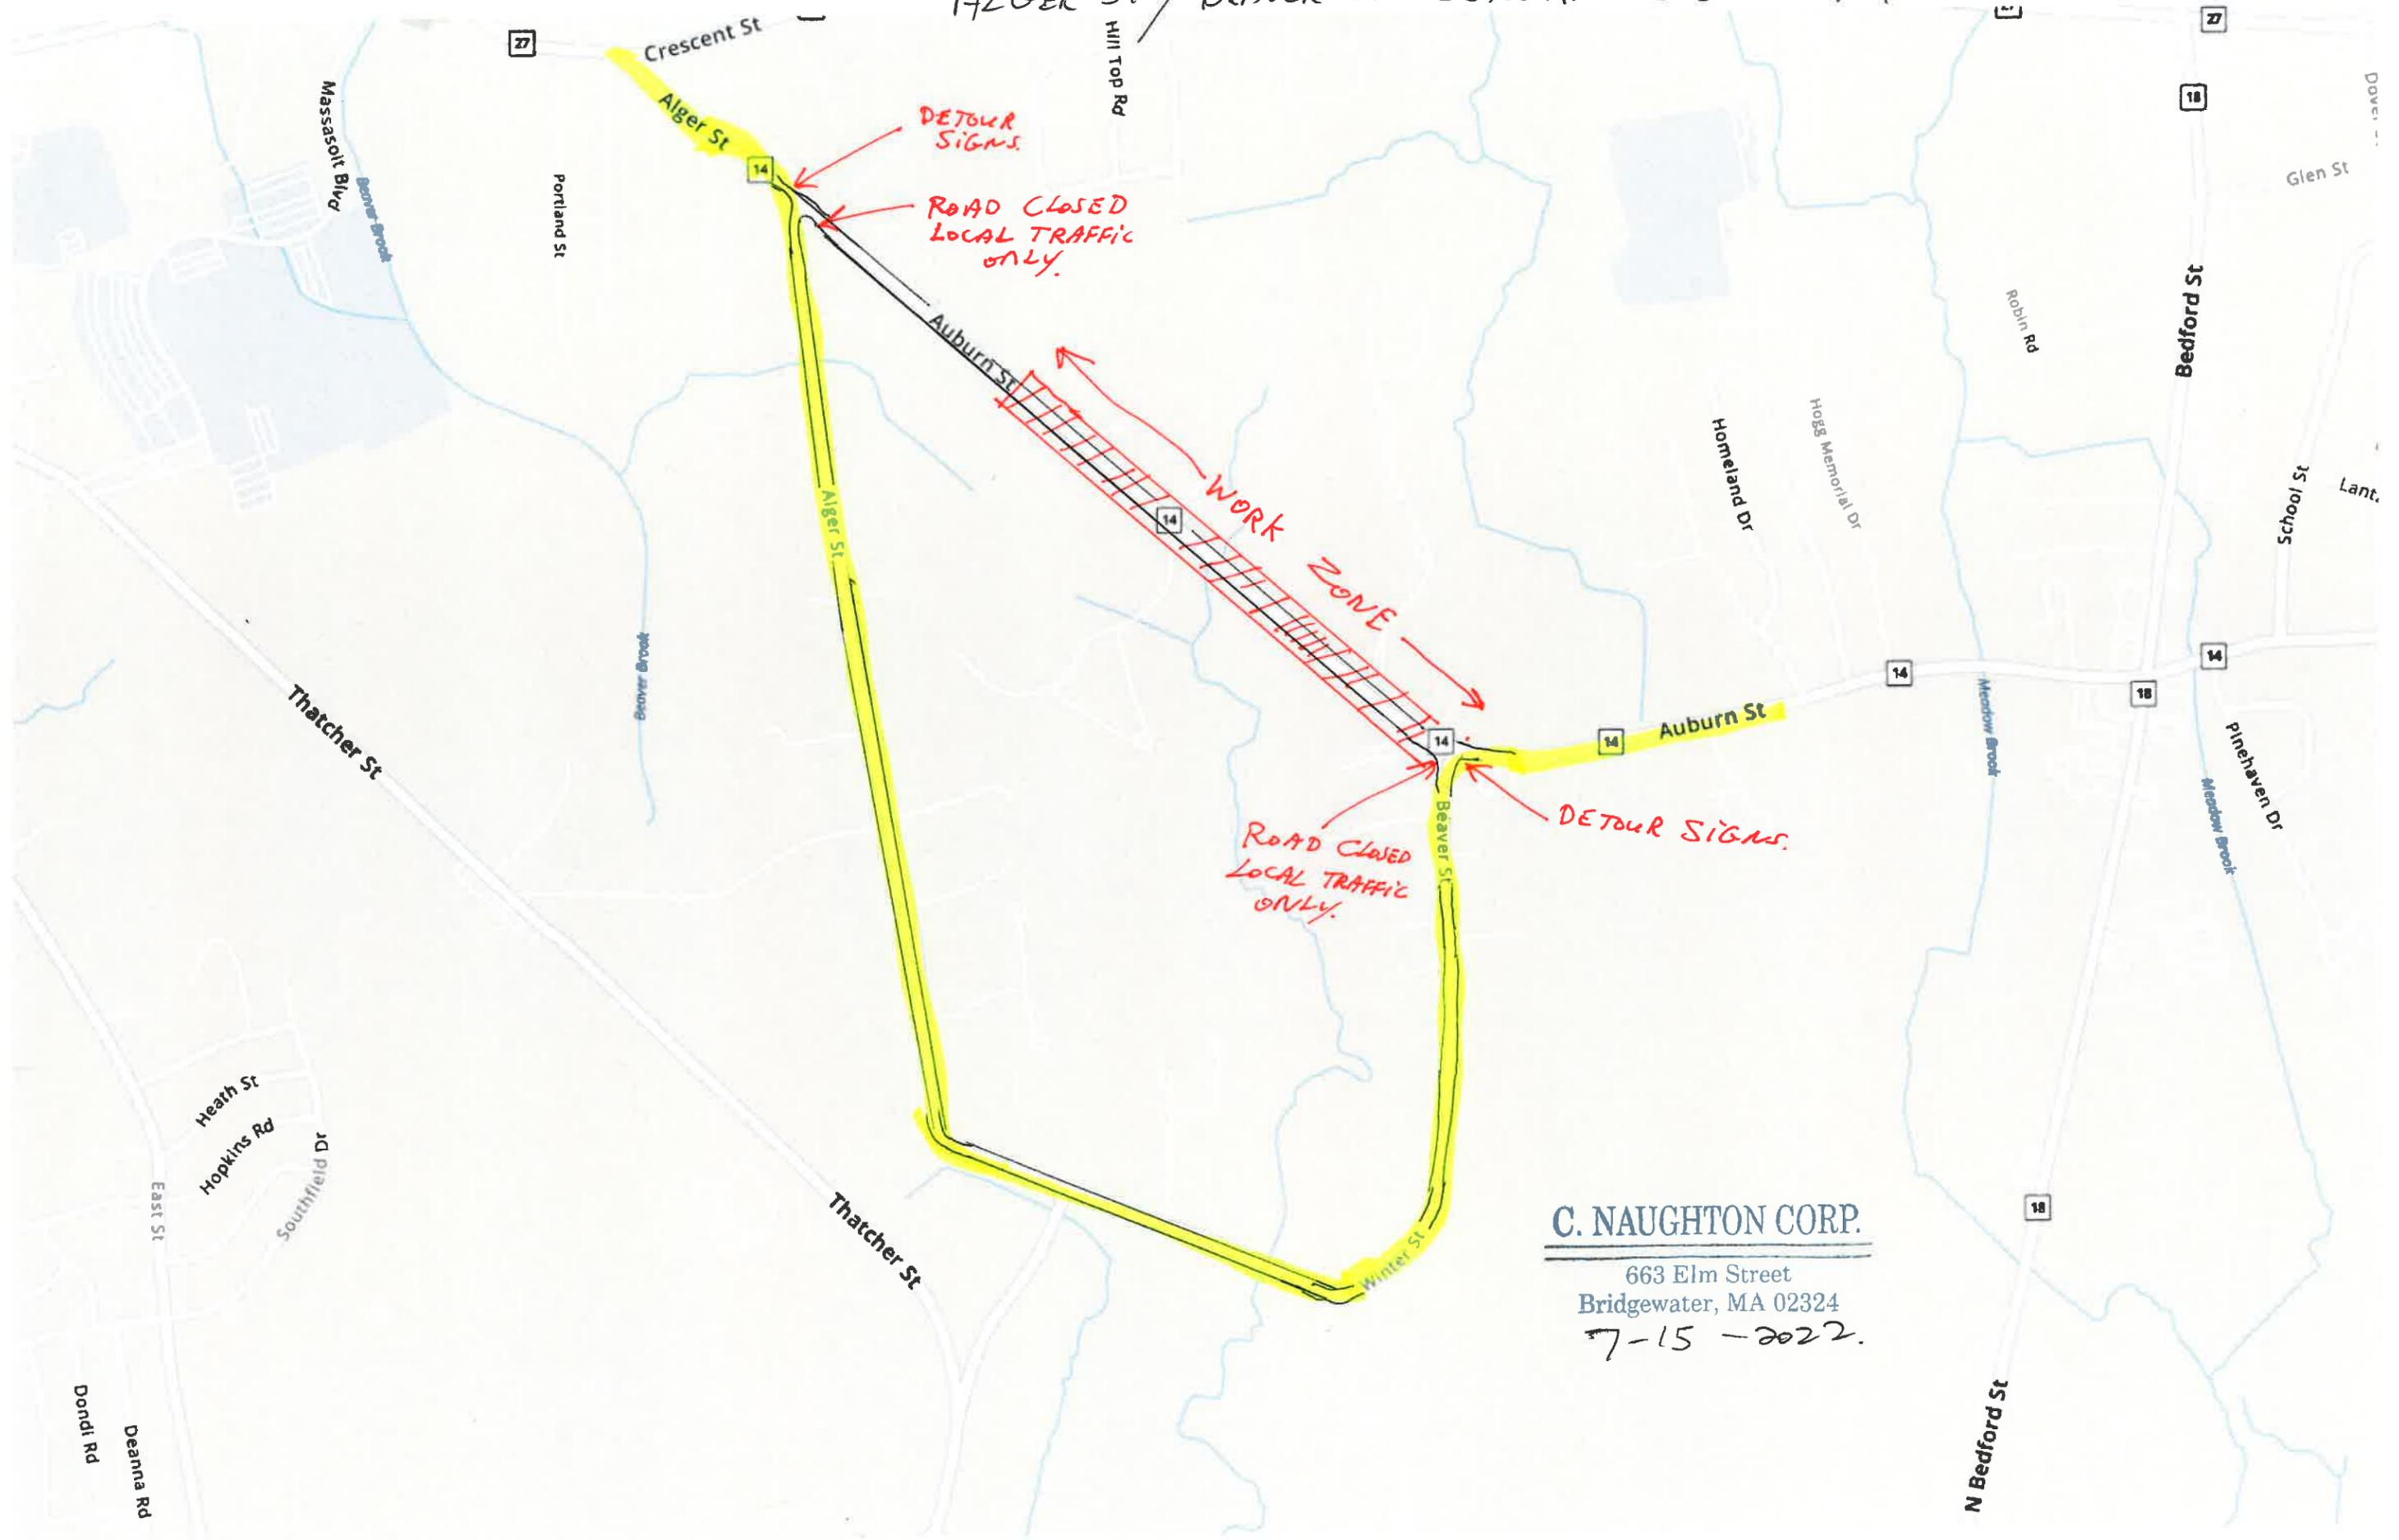

C. NAUGHTON CORP.
663 Elm Street
Bridgewater, MA 02324
7-15-2022.
