




## DAILY WORK & TRAFFIC UPDATE

<b>Project Title:</b> Whitman 20-Inch Force Main Replacement CWSRF - 6885	<b>Date:</b> 9-7-2022
<b>Construction Location:</b> Auburn Street, Whitman, MA	<b>Construction hours:</b> 7 A.M – 5 P.M.
<h3>ANTICIPATED WORK SCHEDULE AND TRAFFIC MANAGEMENT:</h3>	
<ol style="list-style-type: none"> <li>1. C. Naughton has two crews working installing the 12" DI water main and lateral connections today on Auburn Street towards Alger Street. One crew is working just west of Elliot Woods and the other crew is working by the Carousel Family Fun Center.</li> <li>2. There will be alternating single lane traffic at both work locations on Auburn Street. Detour signage is displayed to provide drivers with an alternating route around Auburn Street via Alger Street and Beaver Street. This detour plan is attached.</li> <li>3. Work is expected to take place from 7:00 a.m. until 5:00 p.m. All trenches will be backfilled and paved before leaving for the day.</li> <li>4. Please note, the emergency access gate located at the rear of the middle school parking lot is closed for public access.</li> </ol>	
<b>Prepared By:</b> <u>Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC</u> <b>Reviewed By:</b> <u>Andrew Grota, Project Manager, Environmental Partners Group, LLC</u>	

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

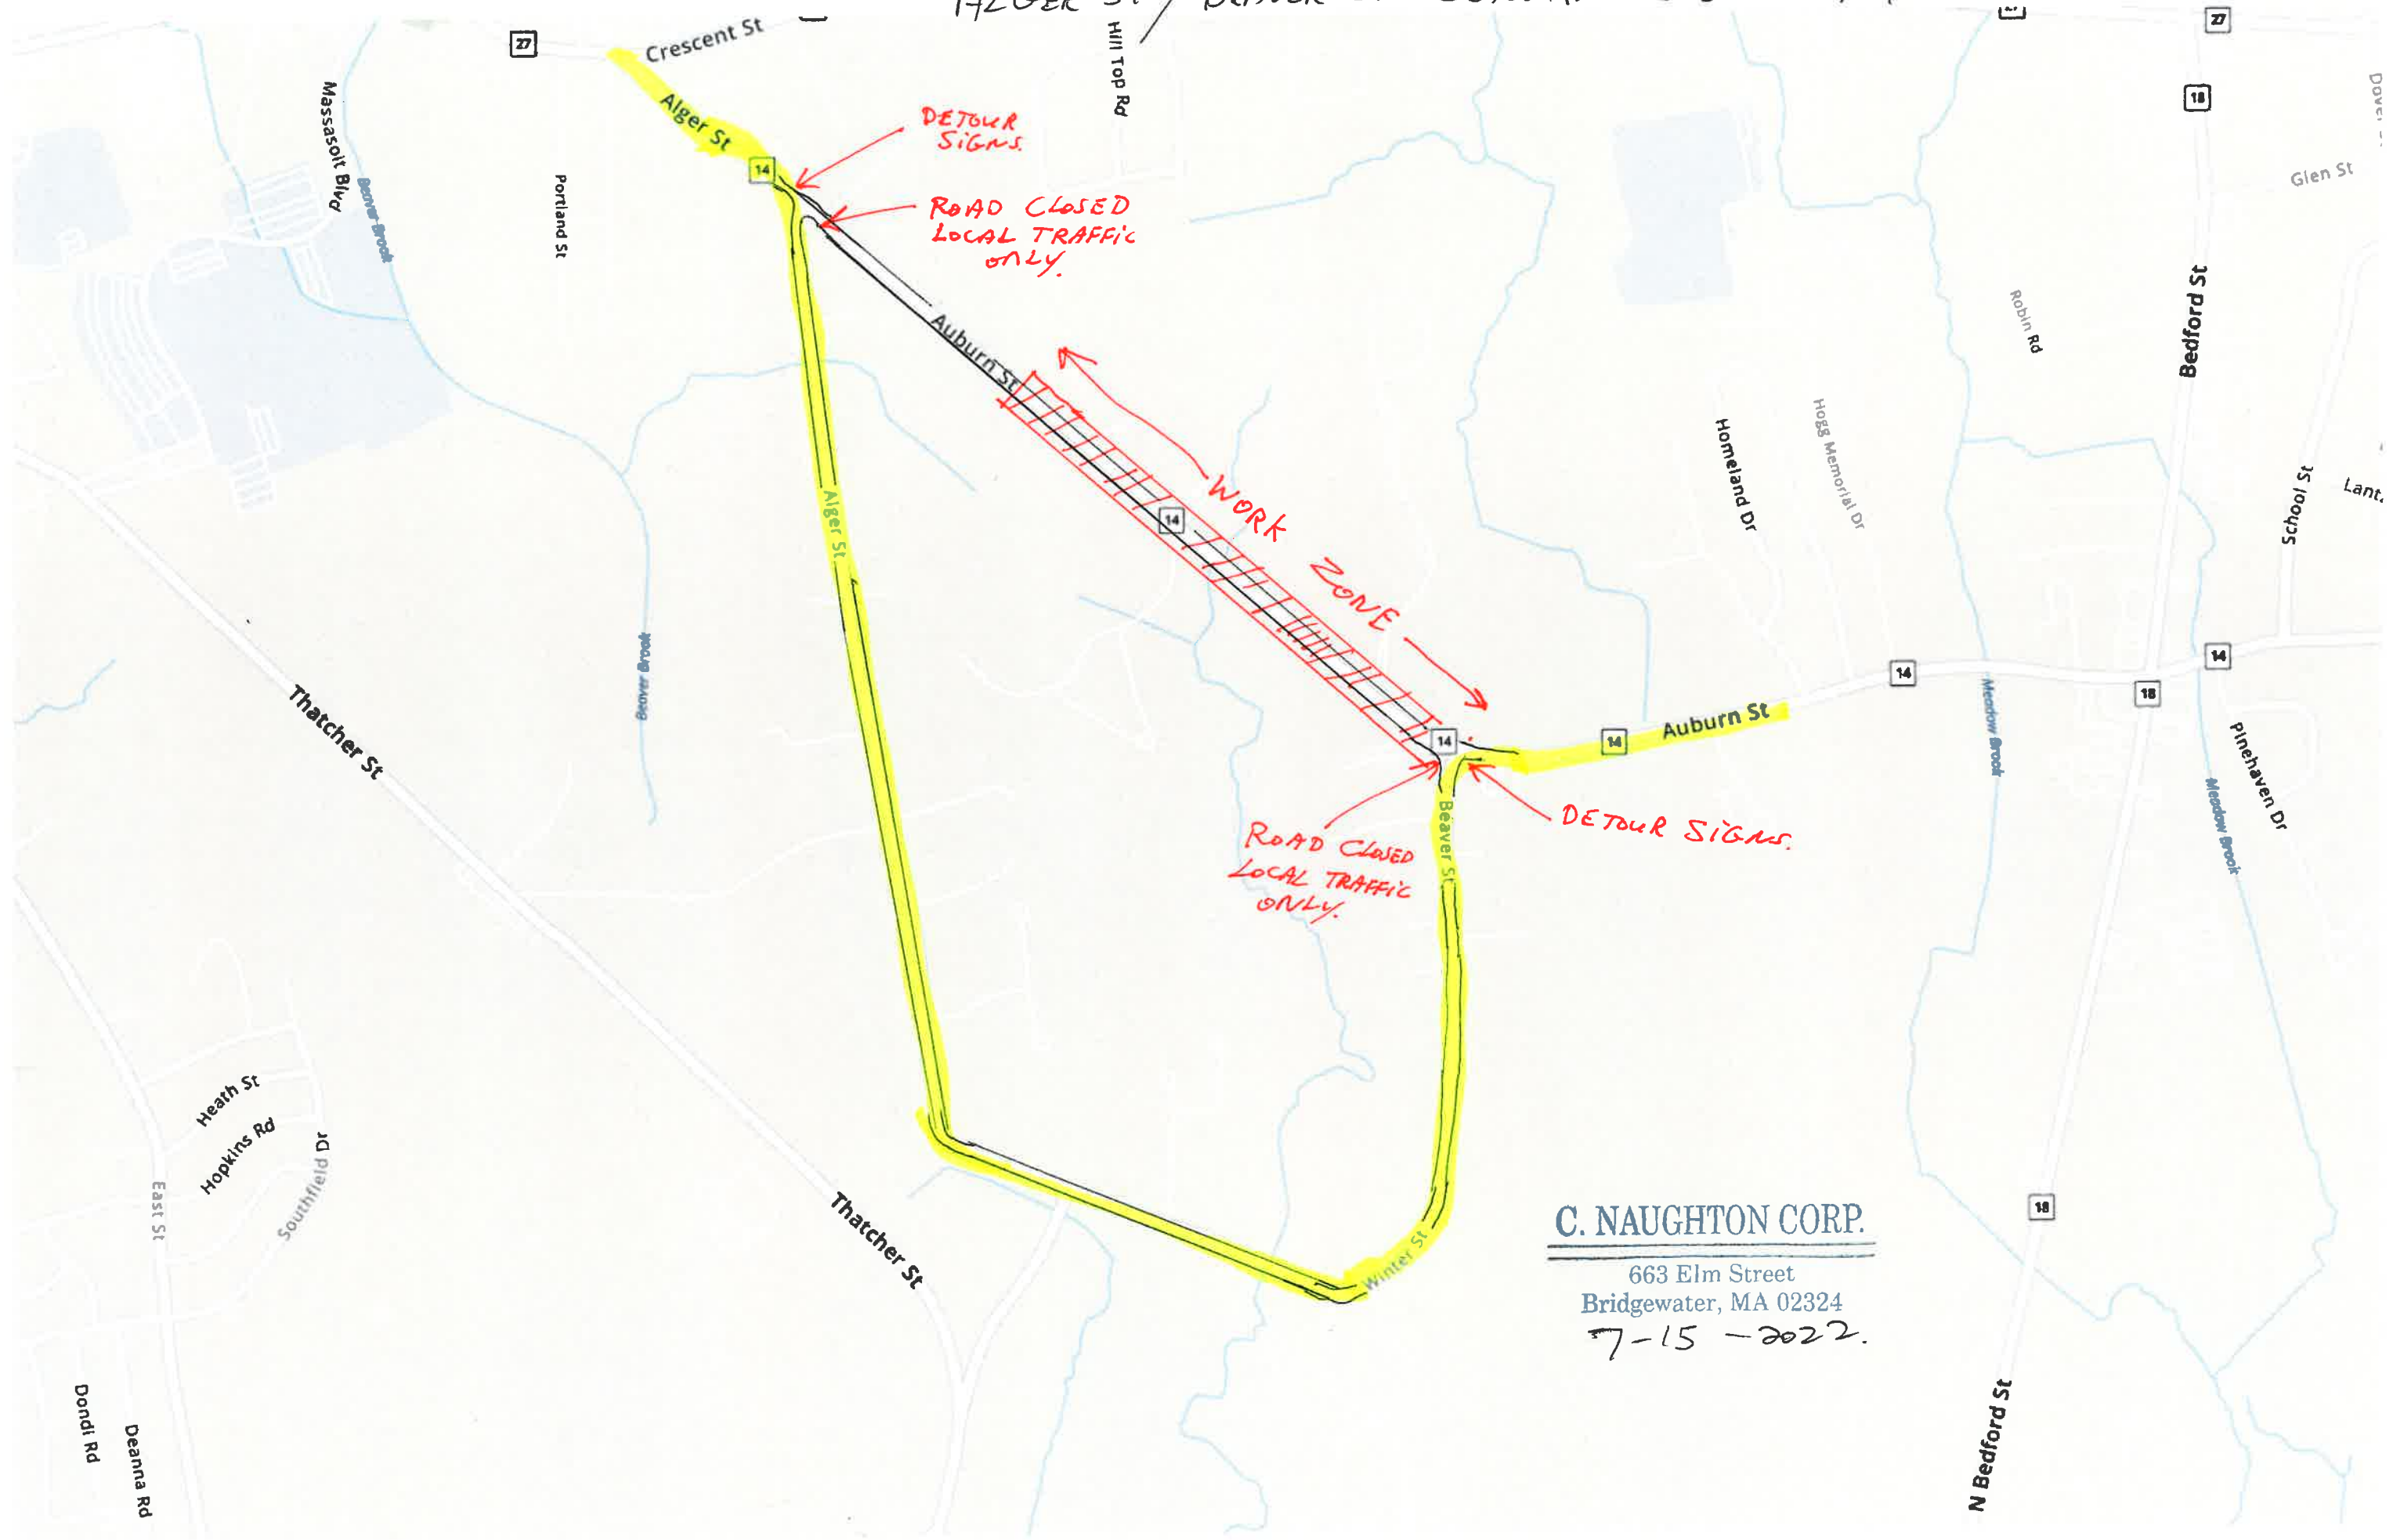

**C. NAUGHTON CORP.**  
663 Elm Street  
Bridgewater, MA 02324  
7-15-2022.
