



WEEKLY CONSTRUCTION UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885		Report #: EP - 09-16-2022
Project Location: Brockton, MA and Whitman, MA	From: 9/12/2022	Week: 22
Client: Whitman, MA	To: 9/16/2022	Engineer Project #: 279-1901
On-Site Engineer: Bob Fitzgerald, Environmental Partners	Contact: (508) 776-7556	
Contractor: C. Naughton Corp.		

CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had one crew continuing the installation of the 20" HDPE sewer force main in the cross-country easement between Auburn St in Whitman and Alger St in Brockton. C. Naughton installed approximately 450 LF of the new 20-inch HDPE sewer force main and associated fittings in the easement. C. Naughton also continued installing timber matting in the cross-country easement this past week.
2. C. Naughton had one crew continuing the installation of the 12" DI water main on Auburn Street. C. Naughton installed approximately 1,000 LF of the new 12-inch DI water main and associated water main gate valves on Auburn Street. Over 80% of the water main is complete on Auburn Street.
3. C. Naughton encountered and damaged the existing 20-inch sewer force main in the cross-country easement in Brockton on Thursday afternoon, 9/15. The sewer main was repaired on Thursday evening and was brought back online on Friday morning.
4. C. Naughton maintained a single lane of alternating traffic on Auburn Street where the water main crew was working with the option for drivers to take an alternate detour route via Alger St.
5. All trenches will be backfilled, compacted, and paved prior to leaving for the weekend.

WEEK LOOK-AHEAD SCHEDULE:

1. C. Naughton will have three crews on site next week (week of 09/19/2022): one crew working in the cross-country easement on the installation of the 20-inch HDPE sewer force main, one crew continuing the installation of the 12-inch DI water main on Auburn Street, and one crew beginning the installation of the 20-inch PVC sewer force main on Southfield Drive.

2. C. Naughton will have Alger Street closed to traffic on Monday, 9/19 and Tuesday, 9/20 in order to cross the roadway with the new sewer force main. C. Naughton will maintain access for local residents and for emergency vehicles while the detour is on-going. Refer to the attached TMP for reference.
3. Daily traffic updates to the Town's project website will be posted to alert residents of anticipated road closures and detours.

PROJECT PHOTOS



Photo 1: View of the Cleared Cross-Country Easement for Installation of 20-inch HDPE Sewer Force Main

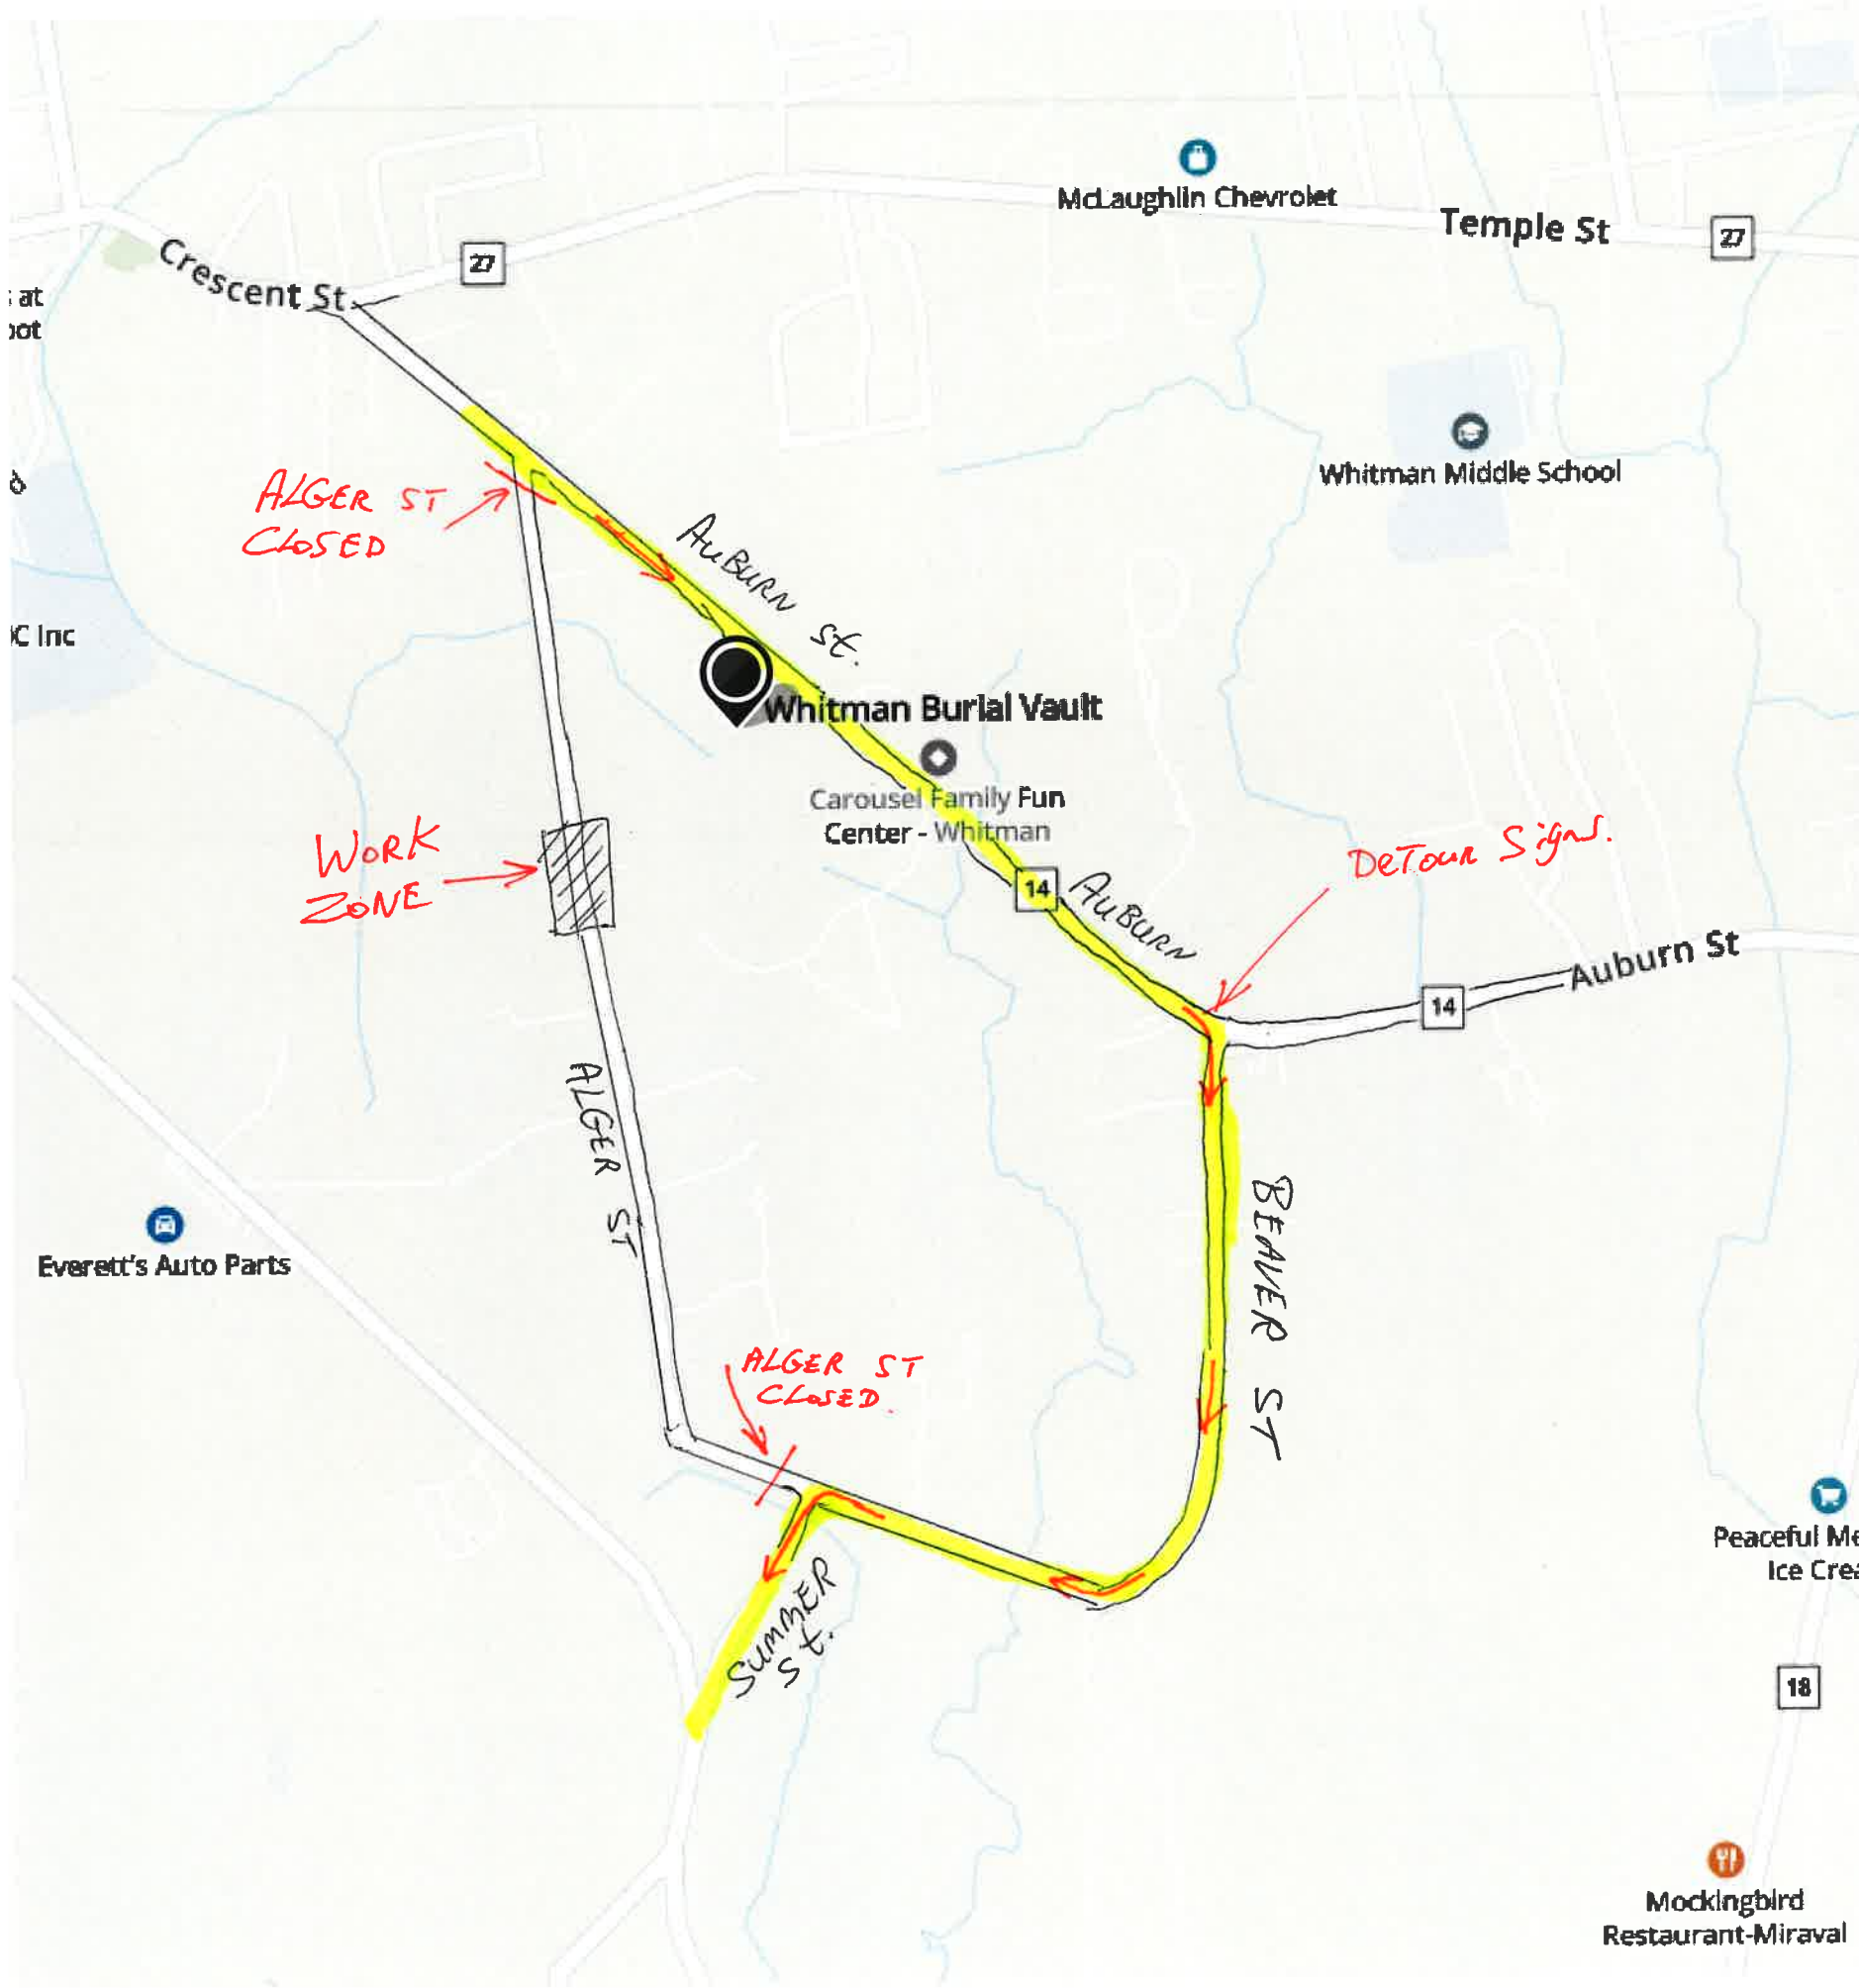


Photo 2: Installation of the 20-inch HDPE Sewer Force Main in Cross Country Easement



Photo 3: Close Up View of the 20-inch HDPE Sewer Force Main in Cross Country Easement

Prepared By: Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC
Reviewed By: Andrew Grotta, Project Manager, Environmental Partners Group, LLC



PROPOSED TRAFFIC PLAN FOR WORK ON ALGER ST.

- ① ALGER ST SHALL BE CLOSED AT THE INTERSECTION OF AUBURN / ALGER ST AND AT THE INTERSECTION OF ALGER / SUMMER ST. ALONG WITH APPROPRIATE SIGNS.
- ② ALGER ST CROSSING WILL BE INSTALLED ON FRIDAY SEPT 16 AND MONDAY SEPT 19.
- ③ WHEN ALGER ST IS CLOSED, TWO WAY TRAFFIC WILL BE ALLOWED ON AUBURN ST ENTIRE LENGTH. THE WATER CREW WILL WORK ON INSTALLING WATER SERVICES ON THE SOUTH SIDE BUT STILL ALLOW 2 WAY TRAFFIC ON AUBURN ST.
- ④ EMERGENCY VEHICLES WILL BE ALLOWED ON ALGER ST AT ALL TIMES.

C. NAUGHTON CORP.

663 Elm Street
Bridgewater, MA 02324

PHIL CASTELLO
9-15-2022
