



WEEKLY CONSTRUCTION UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF – 6885	Report #: EP – 2-10-2023	
Project Location: Brockton, MA, and Whitman, MA	From: 2/6/2023	Week: 42
Client: Whitman, MA	To: 2/10/2023	Engineer Project #: 279-1901
On-Site Engineer: Bob Fitzgerald, Environmental Partners		Contact: (508) 776-7556
Contractor: C. Naughton Corp.		

CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. No work occurred on Monday (2/6/2023).
2. C. Naughton resumed work on Auburn Street on Tuesday (2/7/2023). The crew worked on installing a new 20" DI tee and associated flange joint adaptors inside the new air release manhole near 900 Auburn Street. The crew also installed a new riser and cover at this manhole.
3. On Wednesday (2/8/2023), C. Naughton worked on installing a new 20" DI tee and associated flange joint adaptors inside the new air release manhole near 705 Auburn Street. The manhole concrete top slab was installed, and the trench was backfilled and temporarily paved with asphalt.
4. On Thursday (2/9/2023), C. Naughton worked on installing a new 20" DI tee and associated flange joint adaptors inside the air-release manhole near 1199 Auburn Street. The manhole concrete top slab was installed, and the trench was backfilled and temporarily paved with asphalt. The crew also installed a 4" PVC manhole air vent over towards Utility Pole #90 on Auburn Street.
5. C. Naughton plans on continuing work at the air release manholes on Auburn Street on Friday (2/10/2023). All trenches will be backfilled, compacted, and paved prior to leaving for the weekend.

WEEK LOOK-AHEAD SCHEDULE:

1. No activities are planned for Monday (2/13/2023).
2. C. Naughton plans to resume work on Tuesday (2/14/2023) and will continue the installation of the remaining fittings and valves inside the air release valve manholes along the force main alignment on Auburn Street.
3. C. Naughton anticipates maintaining one lane of alternating traffic on Auburn Street while work is ongoing. Access for residents and emergency vehicles will be maintained during the work.
4. Daily traffic updates to the Town's project website will be posted to alert residents of any planned roadway closures and detours.

PROJECT PHOTOS



Photo 1: New Top Slab at Air Release Manhole



Photo 2: Installation of 20" Ductile Iron Tee Inside Air Release Manhole

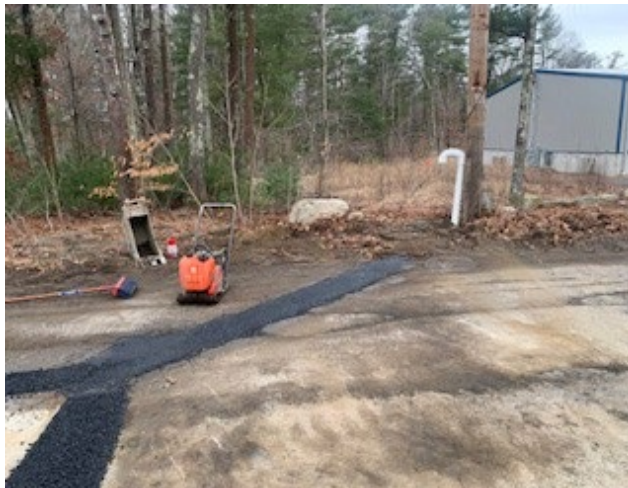


Photo 3: Installation of 4" PVC Manhole Air Vent near Utility Pole #90

Prepared By: Javier Avila, Engineer, Environmental Partners Group, LLC

Reviewed By: Andrew Grota, Project Manager, Environmental Partners Group, LLC
